

1. Rom File Inventory

Stock ROM CIL APRIL-September 2026

PT BULAWAN DAYA LESTARI

No	Date	Sampel ID	Ore Stacking (Dome)	Ore Type - Lithology	Truckcount (m3)	Survey (m3)	Bulk Density	Tonage by survey (WMT)	Toange By Truckcount
1	01/06/2026	G 00290-00313 BB	RP_VM_1	Vein		41	1,35	55	0
2	01/06/2026	G 00272-00279 BB	RP_SV_1	Sandy Oxide		16	1,35	22	0
3	02/06/2026	G 00318-00329 BB	RP_VM-2	Sisa Sandy Oxide		93	1,35	126	0
4	02/06/2026	G 00330-00333 BB	RP_SV_2	Vein		40	1,35	54	0
5	02/06/2026	G 00350-00352 BB	RP_VM_3	Sandy Oxide		13	1,35	18	0
6	15/08/2026		Vein Sandly	Vein Sandly	200	310	1,39	431	278
7	16/08/2026		Bolder Vein	Bolder Vein	220	190	1,39	264	306
8	17/08/2026			Vein	210	34	1,39	47	292
9	18/08/2026			Vein	30	64	1,39	89	42
10	19/08/2026			Vein	60	62	1,39	86	83
11	20/08/2026			Vein	60	108	1,39	150	83
12	21/08/2026			Vein	150	130	1,39	181	209
13	23/08/2026			Vein	110	94	1,39	131	153
14	27/08/2026			Vein	100	310	1,30	403	130
15	28/08/2026			Vein	280	56	1,30	73	364
18	31/08/2026			Vein		23	1,3	30	
22	04/09/2026			Vein		90	1,3	117	
28	10/09/2026			Vein		312	1,3	406	
29	17/09/2026			Oxide Cell A1		2291	1,3	2978	
30	12/09/2026							0	
31	13/09/2026							0	
32	14/09/2026							0	
Average							1,35		
Total					1420	4277		5660	1940

A. Estimasi total tonnage yang masuk dari mining by survey **5660 Ton** update hingga 17 September 2026.

2. Crushing Tonage Production

Crushing Production											
Date	Shift	PIC	Bucket	Type	Moisture %	Volume Bucket	SG Bulk Density (ton/m3)	WMT/SHIFT (wet metrix ton)	DMT/SHIFT (dry metrix ton)	Ton/hour (tph)	Tonage/Day (Tpd)
01/06/2026	Day										-
	Night										
02/06/2026	Day	Toni	141	Exca PC 130	18%	0,5	1,35	95	78	16	78
	Night										
03/06/2026	Day	Toni	32	Exca PC 130	18%	0,5	1,35	22	18	2	18
	Night										
04/06/2026	Day	Deni	282	Exca PC 130	17%	0,5	1,35	190	158	16	158
	Night										
18/08/2026	Day	Adi	62	Exca PC 130	12%	0,5	1,39	43	38	4	38
	Night										
19/08/2026	Day	Adi	463	Exca PC 130	12%	0,5	1,39	322	283	27	283
	Night										
20/08/2026	Day	Adi	539	Exca PC 130	10%	0,5	1,39	375	337	31	337
	Night										
21/08/2026	Day	Adi	409	Exca PC 130	10%	0,5	1,39	284	256	27	291
	Night		10	Loader	10%	2,8	1,39	39	35		
22/08/2026	Day	Adi	315	Exca PC 130	10%	0,5	1,39	219	197	18	197
	Night										
24/08/2026	Day	Adi	234	Exca PC 130	10%	0,5	1,39	163	146	14	164
	Night	Toni	5	Loader	10%	2,8	1,39	19,46	18	2	
27/08/2026	Day	Toni	202	Exca PC 130	11%	0,5	1,39	140	125	12	125
	Night										
28/08/2026	Day	Toni	290	Exca PC 130	11%	0,5	1,3	189	168	16	168
	Night										
29/08/2026	Day	Toni	411	Exca PC 130	10%	0,5	1,3	267	240	22	240
	Night										
30/08/2026	Day	Toni	92	Exca PC 130	10%	0,5	1,3	60	54	5	54
	Night										
10/09/2026	Day	Toni	113	Exca PC 130	10%	0,5	1,3	73	66	6	73
	Night	Toni	2	Loader	10%	2,8	1,3	7	7	1	
11/09/2026	Day										-
	Night										
12/09/2026	Day	Toni	329	Exca PC 130	10%	0,5	1,3	214	192	18	329
	Night	Adit	233	Exca PC 130	10%	0,5	1,3	151,45	136	13	
13/09/2026	Day	Adi	204	Exca PC 130	10%	0,5	1,3	133	119	11	263
	Night	Toni	245	Exca PC 130	10%	0,5	1,3	159,25	143	13	
18/09/2026	Day								-		201
	Night	Toni	360	Exca PC 130	14%	0,5	1,3	234	201	20	
19/09/2026	Day	Toni	178	Exca PC 200	13%	0,7	1,3	162	141	13	322
	Day	Toni	10	Loader	9%	2,8	1,3	36	33	3	
	Night	Toni	250	Exca PC 130	9%	0,5	1,3	163	148	14	
20/09/2026	Day	Toni	50	Exca PC 200	10%	0,7	1,3	46	41	4	210
	Day	Toni	20	Exca PC 130	10%	0,5	1,3	13	12	1	
	Night	Adit	190	Exca PC 200	9%	0,7	1,3	173	157	14	
Rata-rata			203		11%			151	128	13	169
Total			5.671								3.548

- A. Estimasi Tonage yang sudah dilakukan proses crushing material dari Stock Rom CIL hingga tanggal 20 September 2026 adalah **3548 Ton.**

Production Report Processing Plant Agustus-September 2026

Date Start : 31/08/2026

Process To Date : 20/09/2026


3. Carbon in Leach Process and Production Tonnage

Description	Batch 1	Batch 2	Batch 3	Batch 4	Batch 5	Batch 6	Batch 7	Batch 8	Total
	Tank 2	Tank 3	Tank 2	Tank 3	Tank 2	Tank 3	Tank 2	Tank 3	
Material Process (ton)	292	300	327	317	267	277	246	359	2386
Volume Slurry on tank (m ³)	557	539	647	647	647	835	755	970	
Solution (m ³)	421	398	466	473	493	677	615	781	
Gold Au									Rata-Rata
Head grade, ppm	0,708	0,684	0,935	0,929	0,587	0,576	0,536	0,585	0,692
solid tail , ppm	0,056	0,056	0,098	0,109	0,125	0,044	0,100	0,059	0,081
Solution Tail, ppm	0,020	0,030	0,023	0,033	0,026	0,018	0,022	0,027	0,025
% Recovery	88%	86%	86%	83%	71%	85%	71%	80%	81%
Silver, Ag									
Head grade, ppm	0,535	0,793	0,659	0,733	0,497	0,668	0,536	0,588	0,626
Solid tail, ppm	0,170	0,250	0,233	0,240	0,378	0,238	0,147	0,39	0,256
% Recovery	66%	68%	65%	67%	24%	64%	73%	34%	58%
Copper, Cu									
Head Grade, ppm	7,222	9,051	9,069	9,151	9,041	7,580	9,814	10,378	8,913
Solid Tail, ppm	6,550	8,353	8,963	5,163	7,518	7,400	8,167	10,200	7,789
%Recovery	11%	8%	1%	44%	17%	2%	17%	2%	13%
Estimate									Estimasi
Metal Content Recovered (gr)	Batch 1	Batch 2	Batch 3	Batch 4	Batch 5	Batch 6	Batch 7	Batch 8	Total
Gold, Au	182	177	263	244	111	135	94	168	1374
Silver, Ag	116	163	139	156	32	119	96	72	893
Copper, Cu	259	210	35	1264	407	50	405	64	2693

4. Reagent Additional and Reagent Consumption


Penggunaan reagent dan reagent consumption pada process pengolahan area processing plant hingga tanggal 20 September 2026 sebagai berikut :

A. Reagent Additional

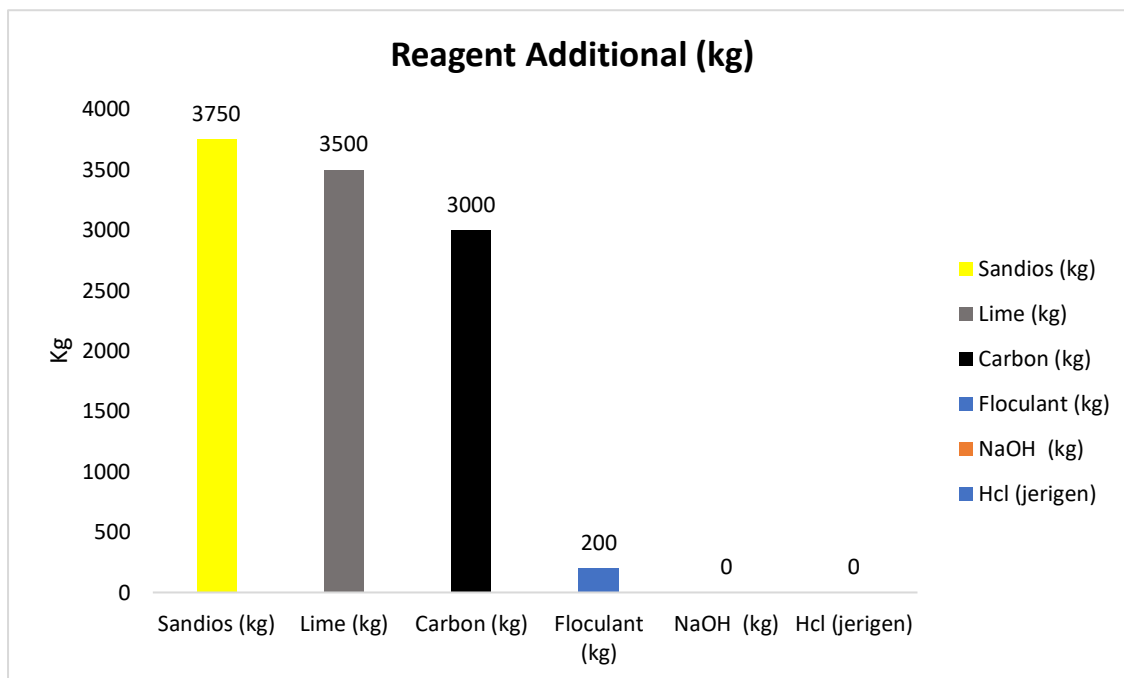

Reagent Additional (kg)					
Sandios (kg)	Lime (kg)	Carbon (kg)	Flocculant (kg)	NaOH (kg)	HCl (jerigen)
3750	3500	3000	200	0	0

B. Reagent Consumption

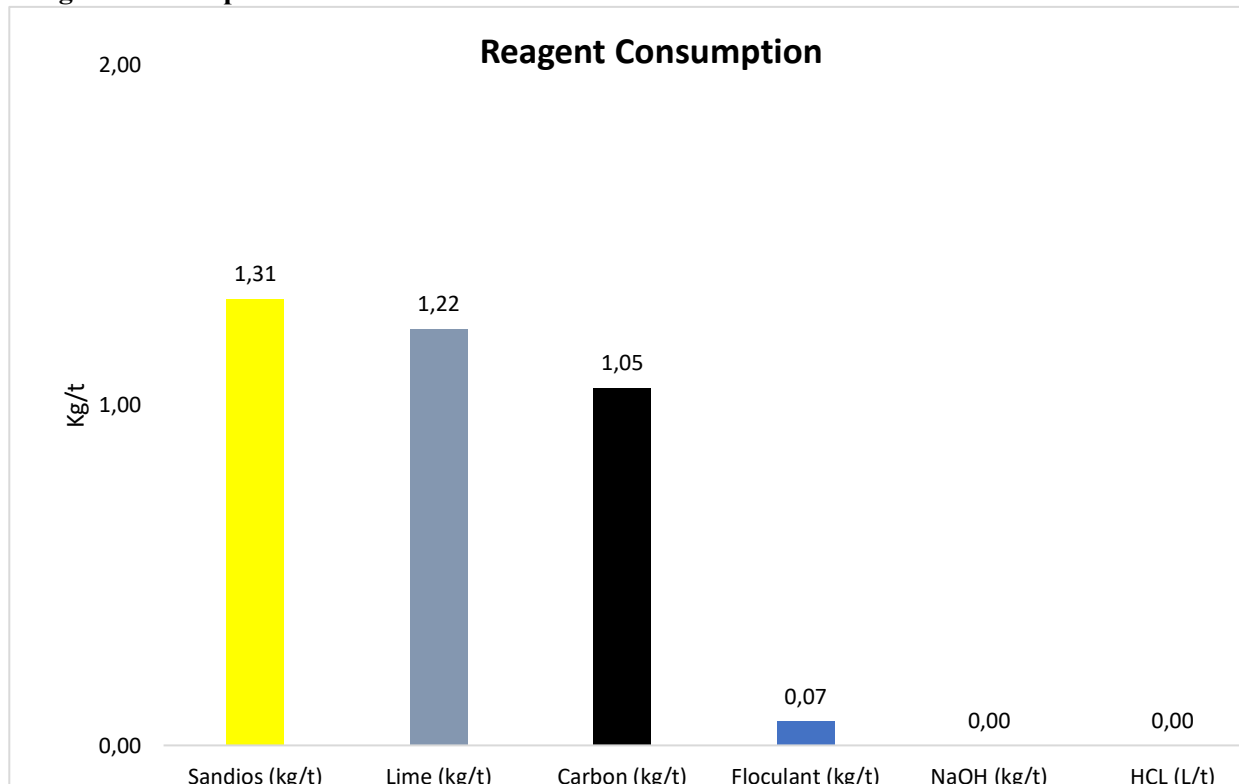


Reagent Consumption					
1,31	1,22	1,05	0,07	0,00	0,00
Sandios (kg/t)	Lime (kg/t)	Carbon (kg/t)	Flocculant (kg/t)	NaOH (kg/t)	HCL (L/t)

5. Plant Availability Grinding Process Ball Mill

A. Running Time and Downtime Grinding Process

Data milling							BATCH	Running Time Hour/Shift	Availability per Shift	Availability Per Day
Date	Shift	PIC	Stop Time	Start Time	Down Time (Mins)	Reason				
31/08/2026	Day	Toni	00:01	01:35	94	Start Ball Mill 1 08:35, start ball mill 2 13:15, start ball mill 3 16:50, ball mill 1,2 dan 3 ada trouble kebocoran dan baud bermasalah	1	10	87%	93%
31/08/2026	Night				0			12	100%	
01/09/2026	Day				0			12	100%	95%
01/09/2026	Night	Toni	00:01	01:07	66	shift malam jam 20:59-21:40 stop thickeener tank bermasalah, jam 06:00-07:00 housekeeping ball mill 3 meluap		11	91%	
02/09/2026	Day	Hadi	00:01	02:01	120	Ball mill sampai jam 12 Cuma berjalan 1, housekeeping material meluap dari ball mill 3 hingga jam 9	2	10	83%	92%
02/09/2026	Night				0			12	100%	
03/09/2026	Day				0			12	100%	96%
03/09/2026	Night	Toni	00:01	01:01	60	Stop ball mill jam 18:00 material finish pump ke tank 3, shift malam drain slurry tank 2		11	92%	
04/09/2026	Day	Hadi	00:01	12:01	720	drain slurry tank 2 dan 3, batch process 1 dan 2		0	0%	0%
04/09/2026	Night	Toni	00:01	12:01	720	drain slurry tank 2 dan 3, batch process 1 dan 2		0	0%	
05/09/2026	Day		00:01	12:01	720	Stop Genset Rusak	3	0	0%	46%
05/09/2026	Night	Toni	00:01	01:01	60	Drain Slurry tank 3, genset 600 dan 750 rusak, ball mill baru mulai shift malam, hanya 1 ball mill dikarenakan genset pakai 300		11	92%	
06/09/2026	Day	Kristo	00:01	04:21	130	Genset mengalami masalah sekitar 120 menit		10	82%	91%
06/09/2026	Night	Yanli			0	Shift malam ada kebocoran pada ball mill 3 jam 06:30, jalan ball mill 1 dan 2		12	100%	
07/09/2026	Day	Toni	00:01	00:20	19	Ball mill no 3 yang baru start jam 09:15, pada jam 13:40 ball mill baru kapasitas 300 tpd mati.		12	97%	94%
07/09/2026	Night	Toni	00:01	01:15	74	Start ball mill 19:30 jalan 2 ball mill no 1 dan 2, jam 21:30 jalan 3 ball mill, no 3 ball mill baru jalan sampai jam 01:45. dari jam 02:25 jalan hanya 1 ball mill, karena genset 750 rusak, hanya pakai genset 300	4	11	90%	
08/09/2026	Day	Toni	00:01	01:41	100	start 1 ball mill jam 07:04 masalah pada genset, start 2 ball mill jam 09:19. ball mill baru no 3 start jam 14:46, ball mill baru no 3 hanya berjalan 3 jam, ada masalah pada pompa dan genset. Efektifitas kerja ball mill adalah no 1 dan 2 running hour mencapai 10 hour		10	86%	82%
08/09/2026	Night	Deny	00:01	02:34	153	start ball mill 1 dan 2, jam 20:33. ball mill baru no 3 start jam 21:08. jam 06:44 ball mill no 2 bocor		9	79%	
09/09/2026	Day	Toni	00:01	09:01	540	Ball Mill Finish pump slurry to tank 3 batch 3, drain slurry tank 2 batch 3		3	25%	13%
09/09/2026	Night	Toni	00:01	12:01	720	Drain Slurry Tank 2 Batch 3	5	0	0%	88%
10/09/2026	Day	Toni	00:01	01:27	86	Start ball mill jam 07:23, jam 09:19-10:23 pompa tank pengental eror		11	88%	
10/09/2026	Night	Septian	00:01	01:33	92	GENSET 750 MATI		10	87%	54%
11/09/2026	Day	Toni	00:01	01:02	61	start ball mill 1 dan 2 sampai jam 15:25. selesai pengisian tank slurry ke tanki no 2 batch pengolahan 5 jam 10:23, ball mill kembali berjalan 12:36 pengisian slurry ke tanki 03 batch pengolahan 6	6	11	92%	
11/09/2026	Night	Toni	00:01	10:01	600	Jalan ball mill 1-2 sampai jam 15:25, jalan ketiga ball mill pada jam 15:25, ball mill 2 mati di jam 17:00 dikarenakan ada kebocoran, pada jam 21:05 ball mill 1,2 dan 3 mati dikarenakan overload material pada tanki thickenner sehingga agitator stuck		2	17%	0%
12/09/2026	Day	Toni	00:01	12:01	720	break down tanki thickenner karena material overload pada tanki thickenner		0	0%	
12/09/2026	Night	Toni	00:01	12:01	720	clean up material overload thickenner tank batch 6 dan pengisian material ke tank 3		0	0%	0%
13/09/2026	Day	Hadi	00:01	12:01	720	Clean up material thickenner dan perbaikan tanki thickenner	7	0	0%	42%
13/09/2026	Night	Toni	00:01	12:01	720			0	0%	
14/09/2026	Day	Toni	00:01	12:01	720			0	0%	100%
14/09/2026	Night	Tony S	00:01	02:01	120	Start Ball Mill jam 20:30	8	10	83%	
15/09/2026	Day	Deny			0	Ball mill jalan 3; ball mill 2 jam 15:35 mati (maintenance di gear grith)		12	100%	96%
15/09/2026	Night	Tony S			0	Ball mill jalan 3; ball mill 2 maintenance, slurry pump to tank 2 batch 7 finish jam 02:39		12	100%	
16/09/2026	Day	Deny			0	Ball mill jalan 3; ball mill 2 maintenance	9	12	100%	100%
16/09/2026	Night	Suono	00:01:00	01:05:00	64	Ball mill 1-2 perbaikan gear grith 00:30, jam 04:00 ball mill 3-4 perbaikan, running lagi 3-4 jam 5		11	91%	
17/09/2026	Day	Yan Lee			0	Running with two Ball Mill (3&4), ball mill 3 sempat bocor & baut longgar, begitupun ball mill 4		12	100%	88%
17/09/2026	Night	Suono			0	Running Ball Mill 3-4. jam 19:20 running ball mill 1,3 dan 4	10	12	100%	
18/09/2026	Day	Septian	00:01:00	02:56:00	175	Kabel putus kena batu mengakibatkan putus aliran listrik dari genset ke pabrik		9	76%	75%
18/09/2026	Night	Awal/Suono	00:01:00	00:01:00	0	Running Ball Mill No 1,3 dan 4		12	100%	
19/09/2026	Day	Yanli	00:01:00	00:01:00	0	Running Ball Mill No 1,3 dan 4	11	12	100%	0%
19/09/2026	Night	Kristo Suono	00:01:00	06:01:00	360	Selesai pengisian tank 2, drain slurry tank 3 tanki flocculant bermasalah		6	50%	
20/09/2026	Day	Toni	00:01:00	12:01:00	720	Flocculation Tank bermasalah drain slurry tank 3 terhambat, ball mill stop	12	0	0%	0%
20/09/2026	Night	Yanli	00:01:00	12:01:00	720	Perbaikan tanki Flocculation		0	0%	

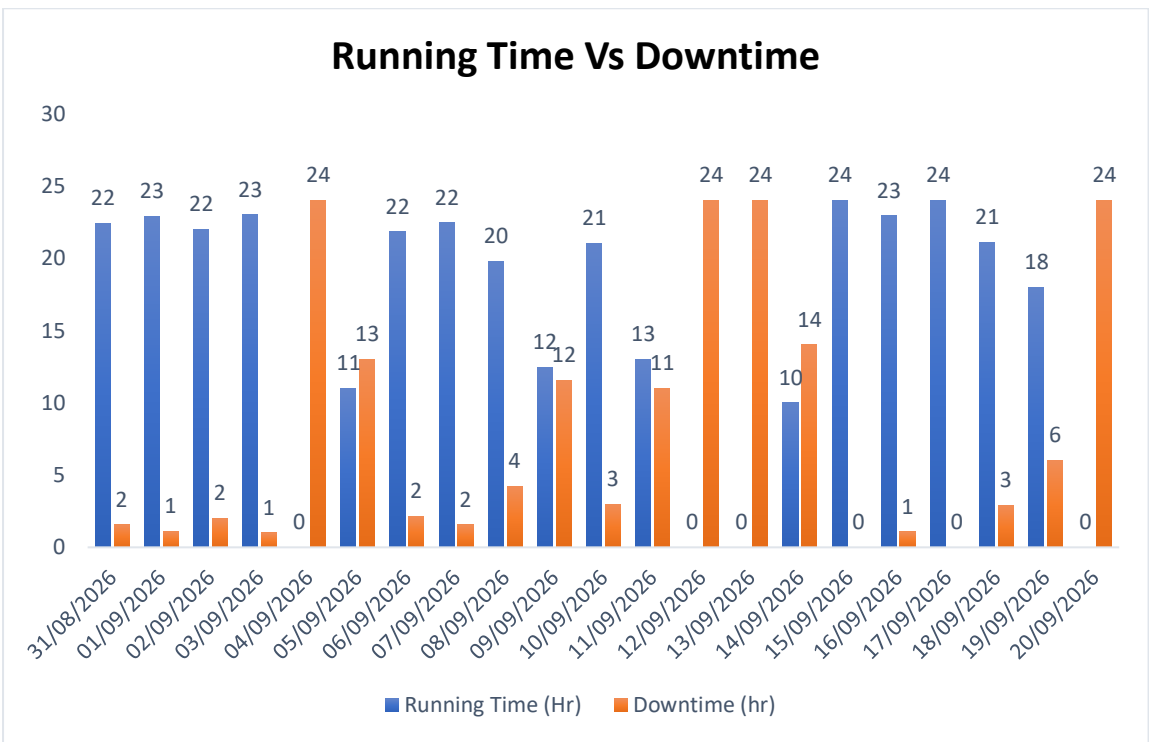

332	172	66%
Running Time Hour Tercatat	Down Time Hour Tercatat	%Plant Availability

Production Report Processing Plant Agustus-September 2026

6. Filter Press Production Estimate

A. Filter Press 01 dan 02 Production Tonnage

Filter Press 01						
No	Date	Shift	Siklus Process	WMT	%Moisture	DMT
1	03/09/2026	Day	16	96	20%	77
2	04/09/2026	Day	5	30	20%	24
3	04/09/2026	Night	12	72	20%	58
4	05/09/2026	Day	10	60	20%	48
5	09/09/2026	Day	4	24	18%	20
6	09/09/2026	Night	12	72	19%	58
7	10/09/2026	Day	4	24	20%	19
8	10/09/2026	Night	3	18	18%	15
9	11/09/2026	Day	8	48	19%	39
10	11/09/2026	Night	4	24	19%	19
11	12/09/2026	Day	7	42	19%	34
12	12/09/2026	Night	11	66	18%	54
13	13/09/2026	Night	10	60	21%	47
14	14/09/2026	Day	9	54	21%	43
15	14/09/2026	Night	6	36	19%	29
16	15/09/2026			0	20%	0
21	17/09/2026	Perbaikan		0		0
22	18/09/2026	Perbaikan		0		0
23	18/09/2026	Perbaikan		0		0
24	19/09/2026	Perbaikan		0		0
25	19/09/2026	Perbaikan		0		0
26	20/09/2026	Day		0		0
27	20/09/2026	Night	6	36		36
28						0

Filter Press 02						
No	Date	Shift	Siklus Process	WMT (Wet Metrix Ton)	%Moisture	DMT (Dry Metrix Ton)
1	03/09/2026	Day	9	108	20%	86
2	04/09/2026	Day	4	48	20%	38
3	04/09/2026	Night	10	120	20%	96
4	05/09/2026	Day	10	120	20%	96
5	09/09/2026	Day	4	48	18%	39
6	09/09/2026	Night	12	144	19%	117
7	10/09/2026	Day	8	96	20%	77
8	10/09/2026	Night	3	36	18%	30
9	11/09/2026	Day	8	96	19%	78
10	11/09/2026	Night	6	72	19%	58
11	12/09/2026	Day	7	84	19%	68
12	12/09/2026	Night	11	132	18%	108
13	13/09/2026	Night	10	120	21%	95
14	14/09/2026	Day	7	84	21%	66
15	15/09/2026	Day	7	84	20%	67
20	17/09/2026	Night	10	120	20%	96
21	18/09/2026	Day	10	120	23%	92
22	18/09/2026	Night	3	36	19%	29
23	19/09/2026	Day	10	120	21%	95
24	19/09/2026	Night	10	120	21%	95
25	20/09/2026	Day		0		0
26	20/09/2026	Night	15	180		180
27	21/09/2026	Day	10	120		120

Estimate Capacity per siklus	
Fp 01	Fp 02
6	12

Total Production
2447

B. Tailing Check Monitoring

Daily Monitoring sandios ppm on Solid Tailing Cake Filter Press

No	Date	Id Sampel	Met Lab Technician	Berat Solid (gr)	FP	V Sampel (ml)	V Agno3 (ml)	M Agno3	Sandios ppm	pH
1	03/09/2026	Filter Press Day Shift	Gerald	1000	1	10	0	0,01	<0,05	7
2	04/09/2026	Filter Press Day Shift	Gerald	1000	1	10	0	0,01	<0,05	7
3	04/09/2026	Filter Press Night Shift	Gerald	1000	1	10	0	0,01	<0,05	7
4	05/09/2026	Filter Press Day	Gerald	1000	1	10	0	0,01	<0,05	7
5	09/09/2026	Filter PressDay	Gerald	1000	1	10	0	0,01	<0,05	7
6	09/09/2026	Filter Press Night	Gerald	1000	1	10	0	0,01	<0,05	7
7	10/09/2026	Filter Press Day	Gerald	1000	1	10	0	0,01	<0,05	7
8	10/09/2026	Filter Press Night	Gerald	1000	1	10	0	0,01	<0,05	7
9	11/09/2026	Filter Press Day	Gerald	1000	1	10	0	0,01	<0,05	7
10	11/09/2026	Filter Press Night	Gerald	1000	1	10	0	0,01	<0,05	7
11	12/09/2026	Filter Press Day	Krisna	1000	1	10	0	0,01	<0,05	7
12	12/09/2026	Filter Press Night	Krisna	1000	1	10	0	0,01	<0,05	7
13	13/09/2026	Filter Press Night	Krisna	1000	1	10	0	0,01	<0,05	7,1
14	14/09/2026	Filter Press Day	Krisna	1000	1	10	0	0,01	<0,05	6,6
15	15/09/2026	Filter Press Day	Krisna	1000	1	10	0	0,01	<0,05	6,8
16	17/09/2026	Filter Press Night	Krisna	1000	1	10	0	0,01	<0,05	7,3
17	18/09/2026	Filter Press Day	Krisna	1000	1	10	0	0,01	<0,05	6,8
18	18/09/2026	Filter Press Night	Krisna	1000	1	10	0	0,01	<0,05	6,7
19	20/09/2026	Filter Press Night	Gerald	1000	1	10	0	0,01	<0,05	7,8
